
# **2C ADVISORY** COMMITTEE

2024 Q2 Report



9/5/2024

**Public Works Department** 

#### AGENDA

- Revenues and Expenditures Update
- Maintenance of Effort Reporting
- Total Program Update
- Program Highlights and Accomplishments
- 2024 Paving Map
- 2024 Paving List
- Before and After Photos



#### Revenues

#### **FINANCE DEPARTMENT**

#### 2C/2C2 Road Tax For Filing Period Ended June 30

	2C - 0.62%					
Month Paid to City	<u>2020</u>	<u>2021</u>	<u>2022</u>	<u>2023</u>	<u>2024</u>	% Over(Under) Previous Year
February	4,198,197	4,234,101	4,722,855	4,861,616	5,107,597	5.06%
March	3,882,045	4,242,383	4,702,443	4,723,856	4,980,606	5.44%
April	4,343,766	5,689,085	6,135,124	6,246,013	5,877,015	(5.91%)
May	3,527,905	5,124,653	5,799,085	5,418,556	5,886,784	8.64%
June	4,393,829	5,239,285	5,607,814	5,829,903	6,145,231	5.41%
July	5,444,453	6,426,629	6,726,707	6,616,829	6,412,650	(3.09%)
Total (Year-to-Date)	25,790,195	30,956,135	33,694,028	33,696,773	34,409,883	2.12%
Refunds						
(Year-to-Date)	218,527	110,247	138,845	248,401	183,307	
Net Revenue						
(Year-to-Date)	25,571,668	30,845,888	33,555,183	33,448,372	34,226,576	


In November of 2019, voters in Colorado Springs passed Issue 2C2, agreeing to continue investment in our roads for years 2021-2025, at a sales tax rate of 0.57%, reduced from 0.62% for Issue 2C that was passed by voters in November 2015, for years 2016-2020.

Filing period is the month the tax monies are collected by the retailer from their customers




#### Revenues and Expenditures



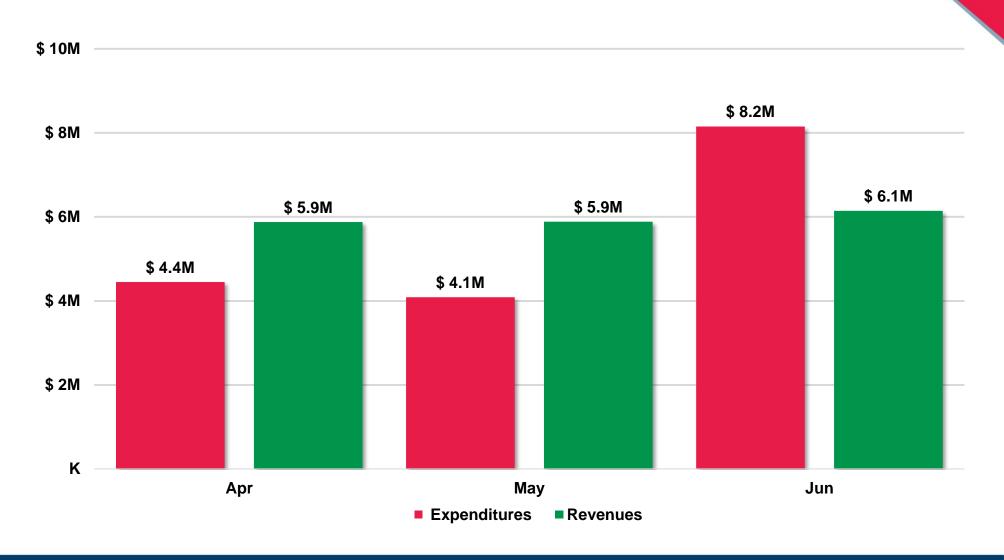

## Revenues and Expenditures Forecast

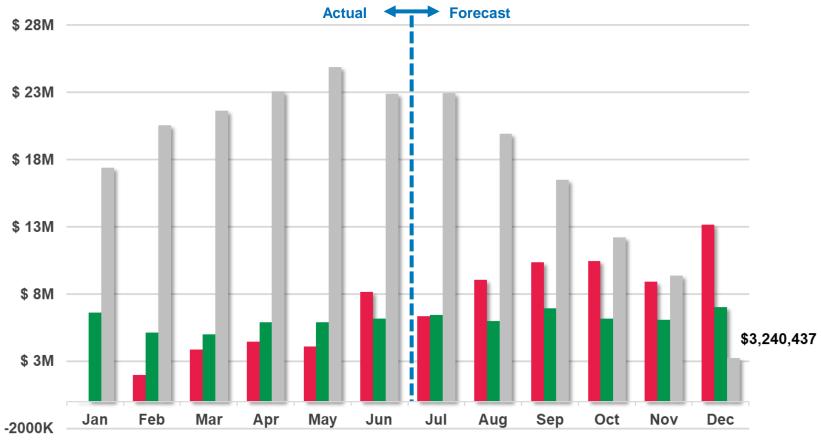




# Maintenance of Effort Requirement



Maintenance of Effort Goal by Quarter											
Quarter		2016	2017	2018		2019	2020	2021	2022	2023	2024
Q2	\$	741,585	\$1,195,643	\$1,082,278	\$	939,325	\$1,362,263	\$1,397,905	\$1,449,986	\$1,734,106	\$ 1,828,314

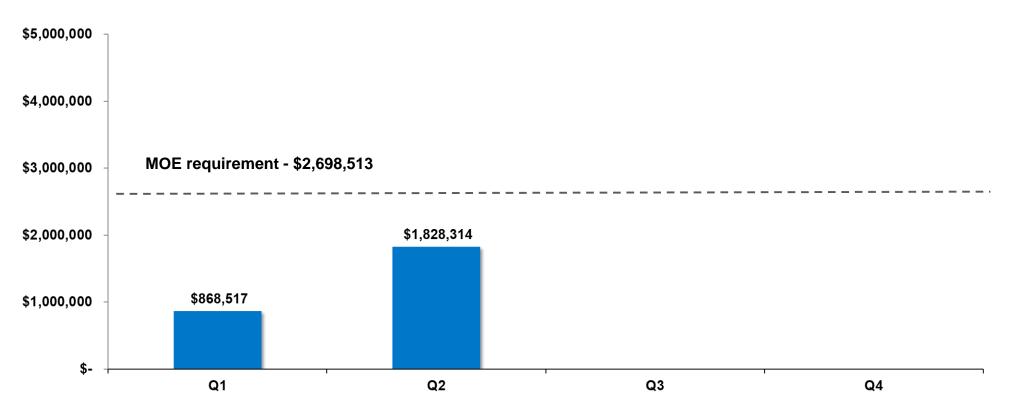

#### **Total Program**


**Q2 Update** 



Program	2C1 Totals	2021	2022	2023	2024 <sup>(3)</sup>	2C2 Totals	Totals
Concrete	\$ 109,821,777	\$ 27,639,604	\$ 46,380,580	\$ 57,474,210	\$ 16,625,739	\$ 148,120,133	\$ 257,941,910
Overlay	127,685,279	19,943,500	15,432,694	28,642,074	3,265,656	67,283,924	194,969,203
Program Support	25,007,650	6,034,028	6,856,688	7,727,218	1,265,674	21,883,608	46,891,258
<b>Total Annual Spend</b>	\$ 262,514,705	\$ 53,617,132	\$ 68,669,962	\$ 93,843,502	\$ 21,157,069	\$ 237,287,665	\$ 499,802,370
Original Budget <sup>(1)</sup>	\$ 257,912,770	\$ 54,599,960	\$ 65,435,820	\$ 70,264,668	\$ 73,588,300	\$ 263,888,748	\$ 521,801,518
Mid-Year Appropriation	\$ 9,000,000	\$ 10,000,000	\$ -	\$ 16,000,000	\$ -	\$ 26,000,000	\$ 35,000,000
Appropriated Budget	\$ 266,912,770	\$ 64,599,960	\$ 65,435,820	\$ 86,264,668	\$ 73,588,300	\$ 289,888,748	\$ 556,801,518
Available to Spend Budget (2)	\$ 301,382,271	\$ 72,927,580	\$ 81,603,146	\$ 99,518,608	\$ 86,768,599	\$ 340,817,933	\$ 642,200,204
Concrete % of Program	42%	52%	68%	61%	79%	62%	52%
Overlay % of Program	49%	37%	22%	31%	15%	28%	39%
Program Support % of Program	10%	11%	10%	8%	6%	9%	9%
% Spend of Available Budget	87%	74%	84%	94%	24%	70%	90%

- (1) Original Budgets will adjusts to actual revenue collections
- (2) Available to Spend Budget includes carryover and purchase order rollover funds
- (3) 2024 expenditures and program % of funding totals do not reflect anticipated 2024 totals
  - Paving Expenditures are recognized in Q3 and Q4 historically
  - Active paving segments will reflect complete by Q4
  - Concrete works on two seasons worth of paving in a given period

## Pre-Overlay Concrete Highlights

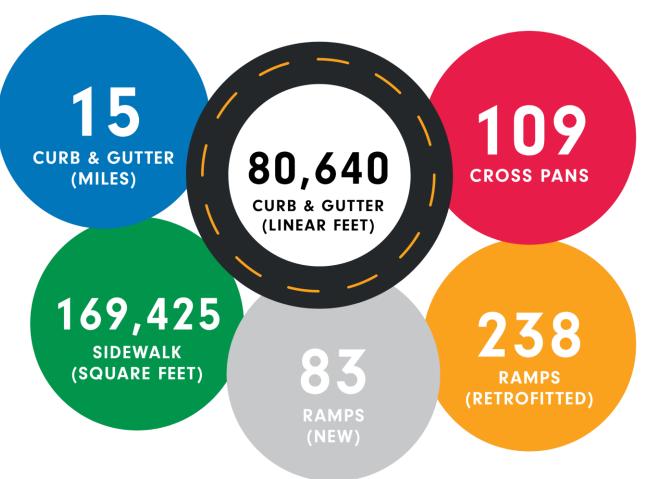



#### **Q2 Highlights**

Sidewalk Placed
Approximately 3 NFL football fields

**Curb And Gutter Placed**Poured the height of Pikes Peak
approximately 5.7 times

### **Asphalt Overlay Highlights**








**56%**Total Program Complete

**152 Lane Miles** Awarded for 2024

# 2024 Paving Map

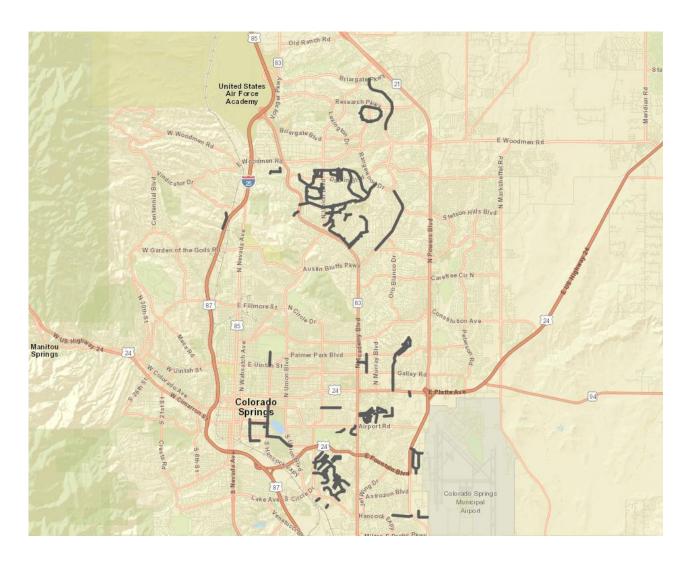



#### **2024 Paving List**

























#### **Questions/Discussion**



Thursday, December 5, 2024

10:30 AM - 11:30 AM

at

City Hall

Pikes Peak Conference Room

Virtual Option Available

